




# Measure V - Clean Beaches and Ocean Parcel Tax

Quarterly Report  
(through June 30, 2016)

*Los Amigos Park hydrodynamic separator unit*



*Los Amigos Park cistern installation*

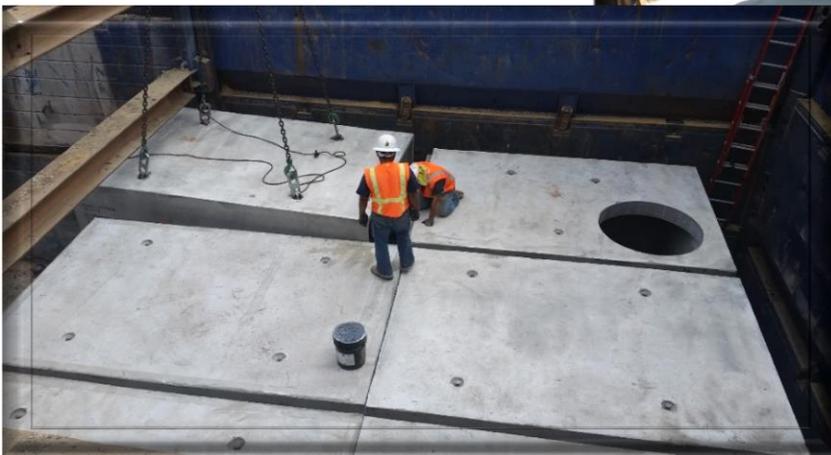

## Citizen's Oversight Committee

Tom Ford, Chair  
Grace Phillips, Vice-Chair  
Benjamin Kay  
Mary Marlow  
William Kairala



Prepared By  
City of Santa Monica  
Civil Engineering Division





# Measure V - Clean Beaches and Ocean Parcel Tax


Section	Page
1.0 Budget Report (CIP) .....	3
Budget Report (Operations) .....	6
2.0 Financial Projection (5 Year Plan) .....	7
3.0 Status Report .....	8

## Budget Highlights

As of the fourth quarter in fiscal year 2015-16, a total of \$7.3M in Measure V funds was appropriated for capital improvement projects. This \$1.1M increase since the March report is due to an increase in costs for the Los Amigos Park project. CIP expenditures in this quarter include \$70K for pervious concrete alley construction, \$62K for pervious concrete gutter construction, \$35K for design of the Marine Park Retrofit Project, \$36K for design of the Los Amigos Park Retrofit Project, and \$11K for construction of the Palisades Park drainage improvements.

Total fund collection\* to date is \$25.4M.  
 Total fund expenditure/allocation\* to date is \$22.8M.  
 Total funds available to date is \$2.6M.

\* since fund inception

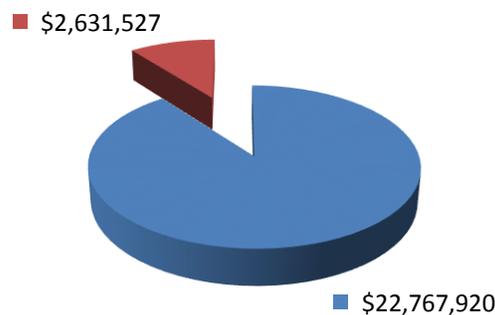



## Measure V - Clean Beaches and Ocean Parcel Tax

Project	Total Budget	Measure V Appropriation	Measure V Expenditure		% Funds Used
			This Quarter	Total through 6/30	

**COMPLETED PROJECTS**

Five Year Plan Preparation		\$153,000.00		\$153,000.00	100%
Water Resource Engineering / Concept Report		\$350,000.00		\$336,790.18	96%
Bicknell Avenue Green Street Project		\$300,000.00		\$94,409.80	31%
Pier Storm Drain Improvements		\$2,169,335.32		\$2,020,308.74	93%
Pier Water Quality Improvements		\$110,754.06		\$110,754.06	100%
Pier Bacterial Source Study		\$60,000.00		\$57,655.05	96%
Ocean Park Blvd Complete Green Street		\$2,018,107.00		\$42,979.79	2%
Regional Bacterial Implementation Plan		\$4,000,000.00		\$4,000,000.00	100%
Storm Drain Inline Infiltration Study		\$325,187.00		\$79,239.17	24%

**C066017.589000 Permeable Surface Alleys - construction of 4' wide pervious concrete centerline gutters in alleys.**

Construction	\$476,773.00	\$476,773.00	\$70,281.62	\$436,797.12	92%
<b>Total</b>	<b>\$476,773.00</b>	<b>\$476,773.00</b>	<b>\$70,281.62</b>	<b>\$436,797.12</b>	

**Measure V Fund Allocation by Phase**



**C066018.589000 Permeable Street Gutters - Construction of pervious concrete street gutters and cross gutters.**

Construction	\$461,773.00	\$461,773.00	\$61,658.97	\$349,431.97	76%
<b>Total</b>	<b>\$461,773.00</b>	<b>\$461,773.00</b>	<b>\$61,658.97</b>	<b>\$349,431.97</b>	

**Measure V Fund Allocation by Phase**






## Measure V - Clean Beaches and Ocean Parcel Tax

Project	Total Budget	Measure V Appropriation	Measure V Expenditure		% Funds Used
			This Quarter	Total through 6/30	

**C066025.589000 Marine Debris TMDL** - Installation of trash screens at catch basins in the Kenter Canyon watershed.

Design / Project Mgmt	\$127,500.00	\$127,500.00	\$6.45	\$8,728.32	7%
Construction	\$537,000.00	\$537,000.00	\$0.00	\$0.00	0%
Construction Management	\$127,500.00	\$127,500.00	\$0.00	\$0.00	
<b>Total</b>	<b>\$792,000.00</b>	<b>\$792,000.00</b>	<b>\$6.45</b>	<b>\$8,728.32</b>	

Measure V Fund Allocation by Phase



**C066022.589000 Marine Park Retrofit** - Retrofit Marine Park to use treated runoff water for irrigation.

Design / Project Mgmt	\$171,000.00	\$171,000.00	\$35,207.05	\$282,412.83	165%
Construction	\$1,720,000.00	\$707,000.00	\$0.00	\$0.00	0%
Construction Management	\$172,000.00	\$172,000.00	\$0.00	\$0.00	
<b>Total</b>	<b>\$2,063,000.00</b>	<b>\$1,050,000.00</b>	<b>\$35,207.05</b>	<b>\$282,412.83</b>	

Measure V Fund Allocation by Phase



**C060265.589000 Palisades Park Drainage Improvement** - Improve drainage and storm drain infrastructure to eliminate park flooding and bluff erosion.

Design / Project Mgmt	\$150,000.00	\$150,000.00	\$0.00	\$56,573.30	38%
Construction	\$750,000.00	\$750,000.00	\$11,252.90	\$306,660.37	41%
Construction Management	\$50,000.00	\$0.00	\$0.00	\$0.00	0%
<b>Total</b>	<b>\$950,000.00</b>	<b>\$900,000.00</b>	<b>\$11,252.90</b>	<b>\$363,233.67</b>	

Measure V Fund Allocation by Phase





## Measure V - Clean Beaches and Ocean Parcel Tax

Project	Total Budget	Measure V Appropriation	Measure V Expenditure		% Funds Used
			This Quarter	Total through 6/30	
<b>C066021.589000 Los Amigos Park Retrofit</b> - Capture offsite runoff, treat and use for irrigation and toilet flushing.					
Design / Project Mgmt	\$150,000.00	\$150,000.00	\$35,662.04	\$154,918.04	103%
Construction - Measure V	\$1,000,000.00	\$652,637.00	\$0.00	\$0.00	0%
Construction Management	\$100,000.00	\$100,000.00	\$0.00	\$0.00	0%
<b>Total</b>	<b>\$1,250,000.00</b>	<b>\$902,637.00</b>	<b>\$35,662.04</b>	<b>\$154,918.04</b>	

Measure V Fund Allocation by Phase



**C069069.589000 Clean Beaches Project** - Capture runoff generated by 85th percentile storm in the Pier watershed and divert to SMURRF for treatment and non-potable use.

Design / Project Mgmt	\$434,840.00	\$323,000.00	\$19.35	\$29.45	0%
Construction	\$4,648,798.00	\$2,154,000.00	\$0.00	\$0.00	0%
Monitoring, outreach	\$82,000.00	\$323,000.00	\$0.00	\$0.00	0%
<b>Total</b>	<b>\$5,165,638.00</b>	<b>\$2,800,000.00</b>	<b>\$19.35</b>	<b>\$29.45</b>	

Measure V Fund Allocation by Phase





## Measure V - Clean Beaches and Ocean Parcel Tax

Description	Account	FY15-16 Budget	Measure V Expenditure	
			This Quarter	through 6/30*1
<b>Salaries and Wages</b>				
Watershed Program Manager*2	06695.533420	\$236,472.00	\$212,875.70	\$893,973.70
Temporary Employees	06402.511500	\$20,913.00	\$0.00	\$9,074.38
<b>Total Salaries and Wages</b>		<b>\$257,385.00</b>	<b>\$212,875.70</b>	<b>\$903,048.08</b>


\*2 FY0809, FY0910 wages/benefits were charged to Measure V Projects. FY1213, FY1314, and FY1415 are fund transfers at the end of FY.

<b>Supplies and Expenses</b>				
Utilities - Telephone	06402.522210	\$658.00	\$16.10	\$2,397.49
Office Supplies	06402.522310	\$532.00	\$0.00	\$4,988.96
Rent	06402.522620	\$37,666.00	\$12,741.98	\$136,241.79
Conference / Meetings / Travel	06402.522820	\$6,617.00	\$0.00	\$29,113.28
Food Purchases	06402.522825	\$0.00	\$0.00	\$1,570.98
Project Maintenance	06402.533090	\$122,160.00	\$6,723.92	\$103,267.60
Indirect Cost Allocation	06402.544340	\$133,713.00	\$33,428.25	\$393,207.00
Contractual Services	06402.555010	\$150,000.00	\$0.00	\$202,021.07
Professional Services	06402.555060	\$132,340.00	\$9,952.48	\$35,624.68
Monitoring Costs	06402.555170	\$205,086.00	\$146,375.00	\$264,751.17
Downspout Redirect Program	06402.560020	\$1,527.00	\$3,235.78	\$4,446.95
Rain Barrel Program	06402.560030	\$13,234.00	\$6,077.89	\$62,368.13
Cistern Program	06402.560040	\$20,360.00	\$2,458.27	\$15,648.27
Tax Exemption - Admin Costs	06402.577110	\$0.00	\$0.00	\$27,536.09
<b>Total Supplies and Expenses</b>		<b>\$823,893.00</b>	<b>\$221,009.67</b>	<b>\$1,283,183.46</b>

Transfer to Stormwater Management Fund (34) - maintenance and upgrade of storm drain infrastructure, SMURRF.

Transfer to 34 Fund	06695.570070	\$411,308.00	\$276,102.30	\$4,980,130.80
<b>Total Transfer to 34 Fund</b>		<b>\$411,308.00</b>	<b>\$276,102.30</b>	<b>\$4,980,130.80</b>

Total Operational Expenditures since inception

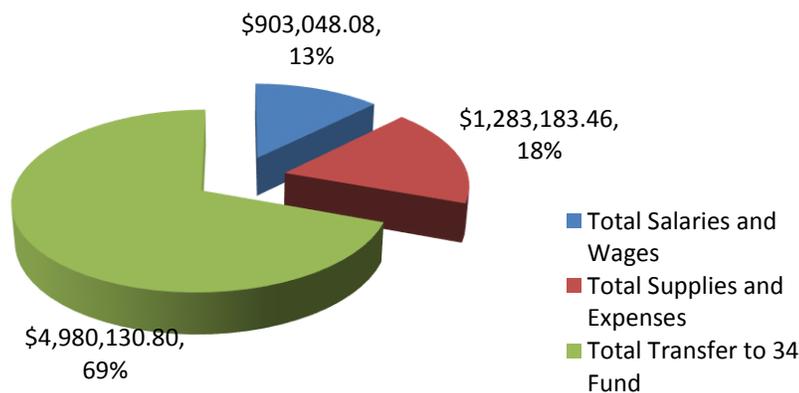


\*1 From inception (7/1/2007) to current



## Measure V - Clean Beaches and Ocean Parcel Tax

	FY14-15	FY15-16	FY16-17	FY17-18	FY18-19
STARTING BALANCE	\$7,447,531.00	\$8,214,032.00	\$2,613,081.00	\$1,371,344.00	\$1,131,713.00
REVENUE	\$2,958,807.00	\$3,001,974.00	\$3,253,543.00	\$3,189,074.00	\$3,259,234.00
PROGRAM ADMIN	(\$330,917.00)	(\$844,806.00)	(\$860,392.00)	(\$874,519.00)	(\$893,608.00)
CIP EXPENDITURE	(\$341,577.00)	(\$7,269,141.00)	(\$370,000.00)	(\$370,000.00)	(\$370,000.00)
TRANSFERS	(\$1,519,812.00)	(\$488,978.00)	(\$964,888.00)	(\$984,186.00)	(\$1,005,838.00)
EWMP PROJECTS			(\$2,300,000.00)	(\$1,200,000.00)	(\$1,000,000.00)
ENDING BALANCE	\$8,214,032.00	\$2,613,081.00	\$1,371,344.00	\$1,131,713.00	\$1,121,501.00

### Fund Balance Projection (5 Year Plan)

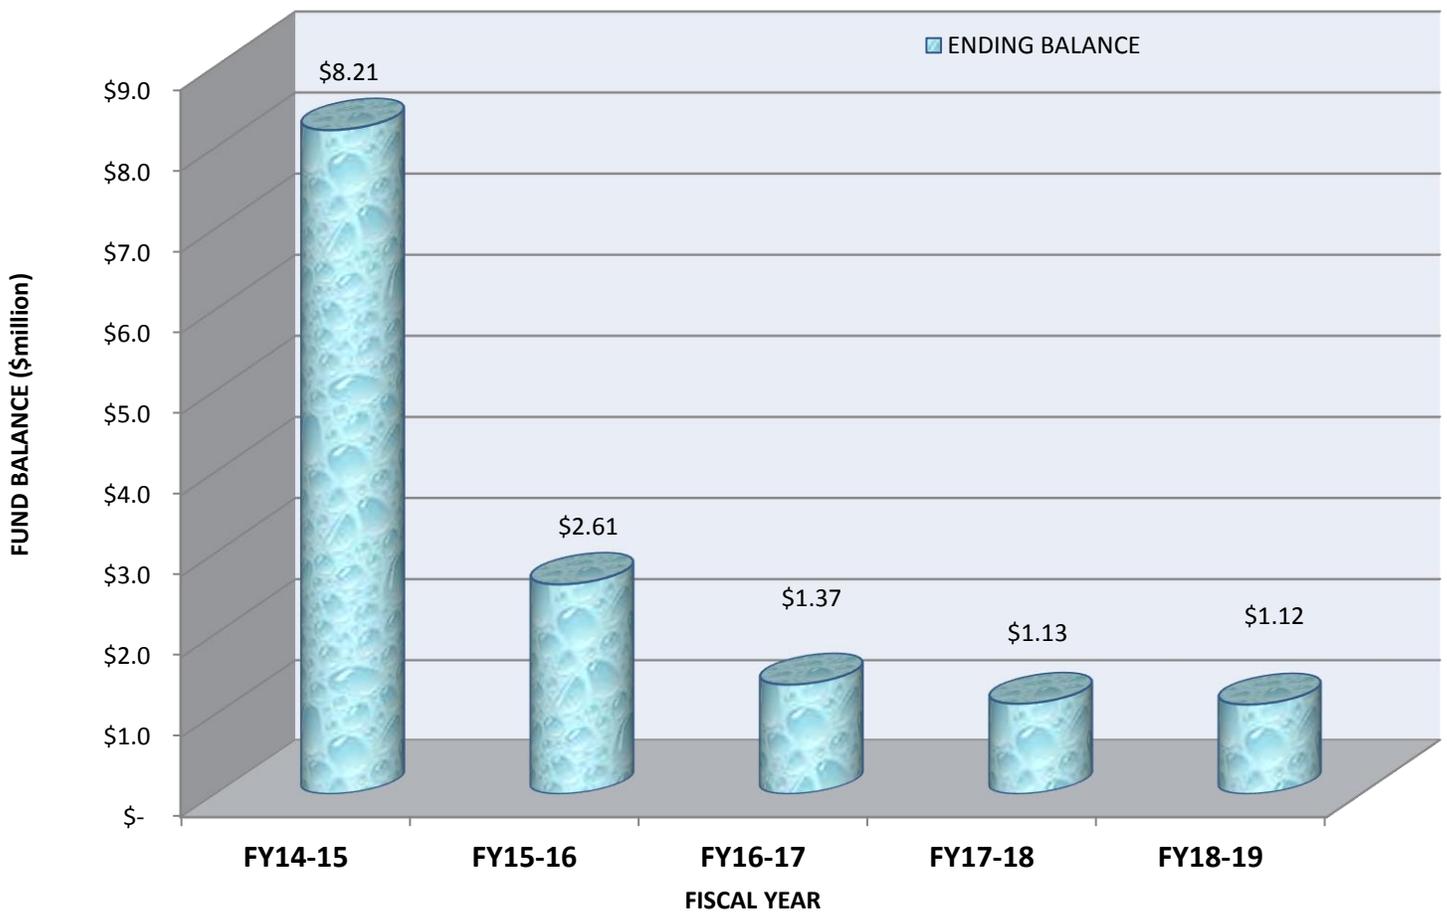



## Measure V - Clean Beaches and Ocean Parcel Tax

Completed Projects	Description
<b>Bicknell Avenue Green Street</b>	This project implemented Best Management Practices such as bio retention cells, pervious concrete parking lanes, subterranean infiltration chambers and filter inserts along Bicknell Avenue between Neilson Way and Main Street. The project is anticipated to infiltrate runoff from a 1.5 acre area. This means that for each 3/4 inch storm event or greater, approximately 30,500 gallons of urban runoff is diverted from the streets into the ground.
<b>Pier Storm Drain Improvement</b>	This project reconstructed the pier storm drain outlet, installed a diversion structure for dry weather flows and replaced 300L.F. of 60" storm drain pipe. This was one of the strategies aiming to improve water quality at the Santa Monica Pier.
<b>Pier Water Quality Improvement</b>	This project installed bird deterrent strategies such as ultrasonic / sonic devices, contraceptive feeding, spikes and netting. The results have been encouraging with reduced number of exceedances and improved beach report card grades from Heal the Bay at the Santa Monica Pier.
<b>Permeable Surface Alleys</b>	The permeable surface alleys are designed to capture some alley runoff and tributary runoff from adjacent private property. <b>FY 10/11:</b> 1400 blk of 14th Ct., 1500 blk of 17th Ct., 1200 blk of 22nd Ct., 1000 blk of 6th Ct., 1200 blk of Lincoln Ct.; <b>FY11/12:</b> 800 blk of 11th Ct., 900 blk of 12th Ct., 1300 blk of 17th Ct., 1200 and 1400 blk of 19th Ct., 900 blk of 6th Ct., 900 and 1200 blk of 7th Ct., 3000 blk of Colorado Place S., 1500 to 1600 blk of Stanford Ct.; <b>FY12/13:</b> 800 and 1000 blk of 12th Ct., 1400 blk of 16th Ct., 1300 to 1500 blk of 18th Ct., 900 blk of 5th Ct., 1200 blk of 9th Ct., 1200 to 1400 blk of Berkeley Ct., 900 blk of Euclid Ct., 1700 blk of Franklin Ct., 1300 blk of Stanford Ct., 1500 blk of Yale Ct.; <b>FY13/14:</b> 900 blk of 10th and 11th Ct., 1000 blk of 10th Ct., 900 blk of Lincoln Ct., 1000 blk of Euclid Ct., 1200 blk of 18th Ct., 1300 and 1500 blk of 19th Ct., 1500-1600 blk of Berkeley Ct., <b>FY14/15:</b> 1300 blk of 12th and 23rd Ct., 2500 and 2600 blk of Wilshire Pl. S., 1200 blk of 25th and 26th Ct.
<b>Permeable Street Gutters</b>	<b>FY11/12:</b> 1700 blk of Pine Street, 700 blk of Pine Street, 200 blk of Hollister Avenue, 200 blk of Mills Street, 200 blk of Beach Street, 100 blk of Pier Avenue; <b>FY12/13:</b> 200-300 blk of 20th Street; <b>FY13/14:</b> 1700 blk of Cedar St., 1700 blk of Maple St.
<b>Ocean Park Boulevard Complete Green Street</b>	This project provided increased sidewalk widths, pedestrian lights, new trees, bikelanes, and stormwater infiltration BMP's such as bioretention, and infiltration pits.
<b>Storm Drain In-line Infiltration Pilot Project</b>	This project evaluated the feasibility of using existing storm drain infrastructure, such as catch basins and manholes, for infiltration purposes. The project installed an infiltration gallery and a drywell connected to existing catch basins and a drywell connected to an existing manhole. The final project report recommended the use of drywells in conjunction with existing catch basins for future BMP strategies.
<b>Palisades Park Drainage Improvements</b>	Palisades Park was subject to localized flooding and runoff from the park over the bluff edge contributed towards erosion along the bluff slopes. This project improved the grading and drainage infrastructure to prevent flooding and runoff over the bluff edges.



# Measure V - Clean Beaches and Ocean Parcel Tax

## Permeable Surface Alleys



**Designer:** City of Santa Monica  
**Contractor:** City Forces  
**Project Manager:** Sylvester Mabry  
**Tel. No:** (310) 458-8505

Alley center swales will be replaced with pervious concrete swales as part of the city's annual alley improvement program.

**PLANNING** 100%  
 Completed  
**CONSTRUCTION**  
 Ongoing on an annual basis

**Location:** Various city alleys

Issues	Alleys planned for FY15/16:
shallow and multiple utilities preclude installation of rock infiltration gallery. Reduced program budget will limit pervious gutters to shorter alley sections instead of full alley length.	1700 blk of 16th Ct 2000 blk of Ocean Pl N 2000 blk of Pearl Pl S 900, 1000, 3100 blk of 5th Ct 2600 blk of Pearl Ct. N
	2200, 2300 blk of 26th ct 2600 blk of Pico Ct S 2900, 3100, 3200 blk of Santa Monica Pl S

## Permeable Street Gutters



**Designer:** City of Santa Monica  
**Contractor:** All American Asphalt  
**Project Manager:** Zach Pollard, PE  
**Tel. No:** (310) 458-8726

Street gutters and intersection cross gutters will be replaced with pervious concrete gutters as part of the city's annual street resurfacing projects.

**DESIGN** 100%  
 Completed  
**CONSTRUCTION**  
 Ongoing on an annual basis

**Location:** Various city streets

Issues	Gutters planned for FY14/15:
	2000 blk of 21st Street



# Measure V - Clean Beaches and Ocean Parcel Tax

## Trash Best Management Practices




Designer: City of Santa Monica  
 Contractor: United Stormwater, Inc.  
 Project Manager: Carlos Rosales  
 Tel. No: (310) 458-2201 ext. 2620

Implementation of trash Best Management Practices at Kenter Canyon watershed to comply with the Santa Monica Bay Marine Debris TMDL. Install Hydrodynamic separators at key storm drain nodal points and full capture screens in remaining catch basins.

**Location:** Various locations throughout Kenter Canyon subwatershed. Total 745 catch basins.

**DESIGN** 100%  
 Design completed  
**CONSTRUCTION** 5%  
 Contract awarded 10/13/2015, catch basin measurements completed, LA County permit is in progress.

**Issues**  
 Fees for retrofitting County owned basins established at \$100-300 catch basin.



## Marine Park Retrofit




Designer: Carrollo Engineers  
 Contractor: TBD  
 Project Manager: Joshua Carvalho  
 Tel. No: (310) 458-2201 Ext. 6461

Construct a recycled water pipeline from Penmar Park in Los Angeles to Marine Park in Santa Monica. Retrofit irrigation system within Marine Park to use treated stormwater from Penmar Park.

**Location:** 1406 Marine Street

**DESIGN** 100%  
 Completed  
**CONSTRUCTION** 0%  
 Permitting process: LA BOE, LA SAN, LA Rec & Parks, LA County DHS

**Issues**  
 Negotiating MOA with City of Los Angeles Bureau of Sanitation for use of treated water.  
 LA R&P Commission - approved easement, need execution  
 LA Bureau of Engineering - approved design  
 LACDPH - approved  
 SM B&S - approved

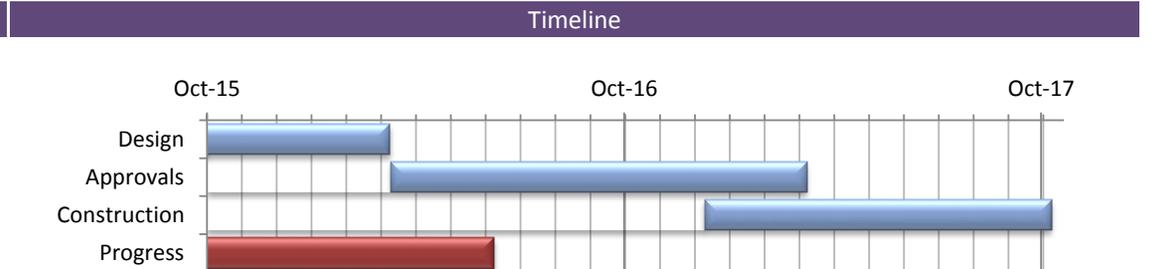



# Measure V - Clean Beaches and Ocean Parcel Tax

## Los Amigos Park Retrofit




**Designer:** California Watershed Engineering  
**Contractor:** TBD  
**Project Manager:** Carlos Rosales  
**Tel. No:** (310) 458-8721 ext. 2620  
**Location:** 500 Hollister Ave.

Divert dry and wet weather runoff from an existing storm drain into the park to be treated and used for non-potable purposes such as irrigation and toilet flushing.

**DESIGN** 100%  
 Completed  
**CONSTRUCTION** 0%  
 Construction bid package was posted. Bids due on 4/19/2016.

**Issues**  
 Requires review by DSA, County Public Health, LA County Flood Control District, SMMUSD.  
 SMMUSD utility easement approved.



## Clean Beaches Project for Pier and Kenter Canyon Basins



**Designer:** TBD  
**Contractor:** TBD  
**Project Manager:** Selim Eren  
**Tel. No:** (310) 458-2201 Ext 5107  
**Location:** Deauville lot. Parcel north of the City beach maintenance yard (north of Santa Monica Pier).

The project captures the runoff from the Pier drainage basin generated by an 85th percentile 24 hour storm event. The project will also capture some runoff from the Kenter Canyon drainage basin. Captured runoff will be stored in a tank and supplied to the SMURRF for treatment and subsequent non-potable use.

**DESIGN** 0%  
 Design contract award on 4/12/2016  
**CONSTRUCTION** 0%

**Issues**

